

Original schedule		
Project:	County: Cherokee	Route/Road :014000
Description: SR 140 FROM I-575 TO CR 777/ARNOLD MILL ROAD		

A. SUMMARY OF UTILITY FACILITIES AND UTILITY ADJUSTMENT SCHEDULE.

List of all existing facilities within project (exclude minor items)

Quantity, Type of facility, Type of service	Quantity in conflict	Units
transfer to 5 new Ga. power poles	5	EA

Existing facility locations were identified using **Record/Map Field Review** dated: **May 25, 2021**

This schedule is based on **Revision** dated: **May 20, 2021**


If any changes are made to the plans after this date, which affect the utility, then this schedule may require modification.

Prepared by	Title	Phone	Date
<i>pete hughes</i>	<i>staking tech</i>	<i>404-403-3007</i>	<i>May 25, 2021</i>
Approved by GDOT	Title	Phone	Date

Comments


B. SPECIAL REQUIREMENTS (staging required, dependent activities, joint-use coordination, etc.).

none

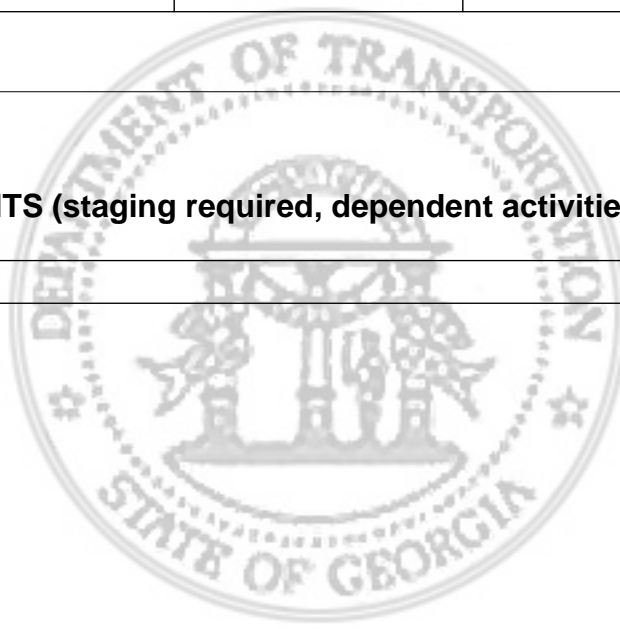

C. WORK PLAN - provide disposition of all existing and proposed facilities on project.

Location	Description of utility work	Dependent activities	Plan Stage No.	Days	Average number of workers
Preliminary Engineering					
STATION# 10+00 THRU STATION #25+00	REVIEW FINAL PLANS AND VERIFY CONFLICTS	RECIPT OF FINAL PLANS AND FULL NOTICE TO PROCEED	NA	3	1
Construction Engineering					
STATION # 10+00 THU STATION # 25+00	VERIFY NEW POLE LOCATIONS AND DEVELOP STAKING STEETS	PRELIMINARY ENGINEERING , FULL NOTICE TO PROCEED GA POWER SET NEW POLES, SCHEDULING	1	21	1
Construction					
STATION # 10+00 THU STATION # 25+00	RELOCATED SAWNEE FACILITIES TO NEWLY RELOCATED GA POWER POLES	CONSTRUTIO N ENGINEERING	1	15	6



D. SCHEDULE SUMMARY FOR WORK PLAN.

Exclude weekends, weather delays and non-productive time:

Work Phase	Total estimated days	Prior to project award	After project award
Preliminary Engineering	3		4
Construction Engineering	21		25
Construction	15		41

Project duration for non-concurrent activities in days: 41

